

Transmission Projects Update

NPPD Board of Directors

Board Meeting


August 9, 2018



Nebraska Public Power District

Always there when you need us

R-Project 345 kV Transmission Line

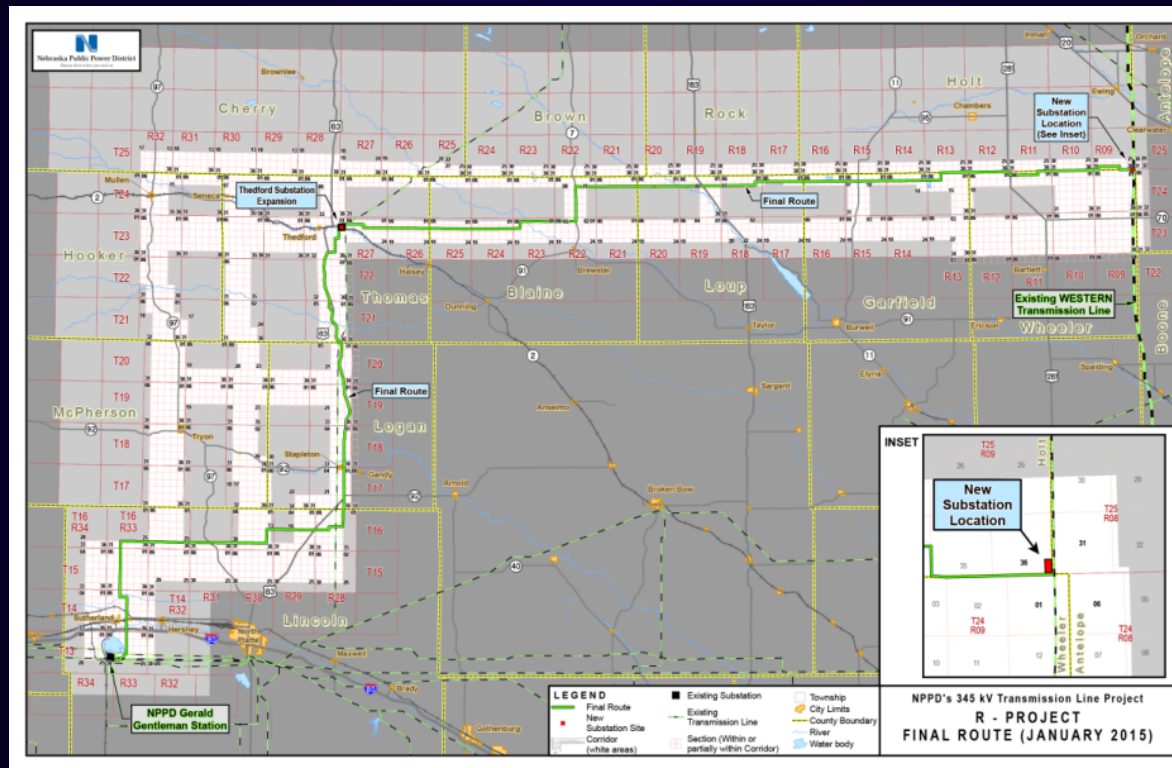

≡ R-Project 345 kV Transmission Line

- **Easement Acquisition:**
 - Easement packages released for acquisition – 632 of 632 (100%)
 - Easements acquired – 418 of 632 (66%)
 - 136 of 225 miles of right-of-way acquired (60%)
 - 133 of 179 (74%) landowners have signed easements
- **Continue to acquire Tension and Pull Sites**
 - 35 of 51 acquired (69%)
- **Continue to acquire Storage and Fly Yards**
 - 21 of 26 acquired (84%)

≡ R-Project 345 kV Transmission Line

- U.S. Fish & Wildlife Services hosted a public hearing on the Programmatic Agreement on July 25, 2018 in North Platte
- The second round of Cultural Surveys were conducted from July 11-18, 2018
 - Third round to begin August 21, 2018
- American Burying Beetle Survey scheduled for August 1-6, 2018
- Project Team continue to address construction contract questions and clarifications from potential bidders

≡ R-Project 345 kV Transmission Line

- **Milestones:**
 - **Final Line Route Announcement – January 2015**
 - **Began Easement Acquisition – December 2015**
 - **Begin Construction – December 2018***
 - **In-service – Approximately two years after construction starts**

*No sooner than receiving record of decision from U.S. Fish & Wildlife Services
