

Transmission Projects Update

NPPD Board of Directors

Board Meeting


July 12, 2018



Nebraska Public Power District

Always there when you need us

R-Project 345 kV Transmission Line

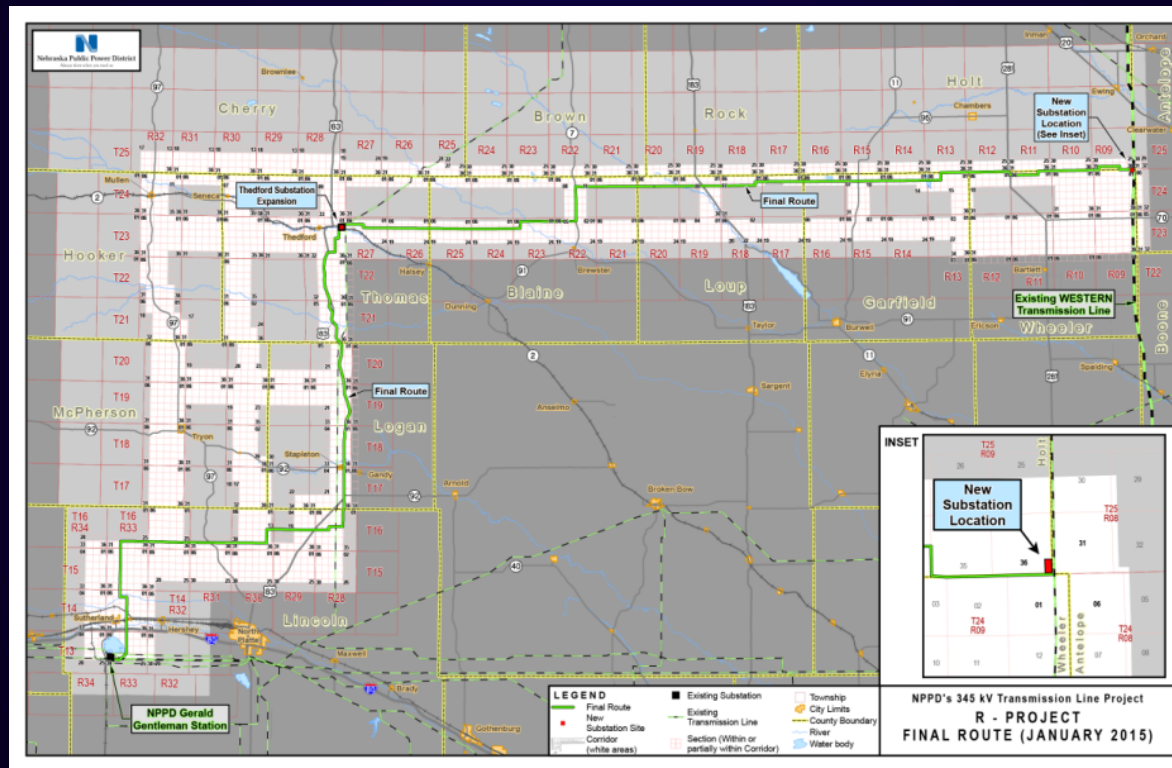

≡ R-Project 345 kV Transmission Line

- **Easement Acquisition:**
 - Easement packages released for acquisition – 632 of 632 (100%)
 - Easements acquired – 418 of 632 (66%)
 - 136 of 225 miles of right-of-way acquired (60%)
 - 133 of 179 (74%) landowners have signed easements
- **Continue to acquire Tension and Pull Sites**
 - 35 of 50 acquired (70%)
- **Continue to acquire Storage and Fly Yards**
 - 20 of 26 acquired (77%)

≡ R-Project 345 kV Transmission Line

- Construction pre-bid meeting was conducted on June 27, 2018, in Columbus
- The first round of Cultural Surveys was conducted from June 20-27
- Orchid surveys were conducted June 25-27
- American Burying Beetle Survey scheduled for August
- Wetland Surveys scheduled for August/September timeframe

≡ R-Project 345 kV Transmission Line

- **Milestones:**
 - **Final Line Route Announcement – January 2015**
 - **Began Easement Acquisition – December 2015**
 - **Begin Construction – December 2018***
 - **In-service – Approximately two years after construction starts**

*No sooner than receiving record of decision from U.S. Fish & Wildlife Services
