

Transmission Projects Update


NPPD Board of Directors
Board Meeting
September 13, 2018



Nebraska Public Power District

Always there when you need us

R-Project 345 kV Transmission Line

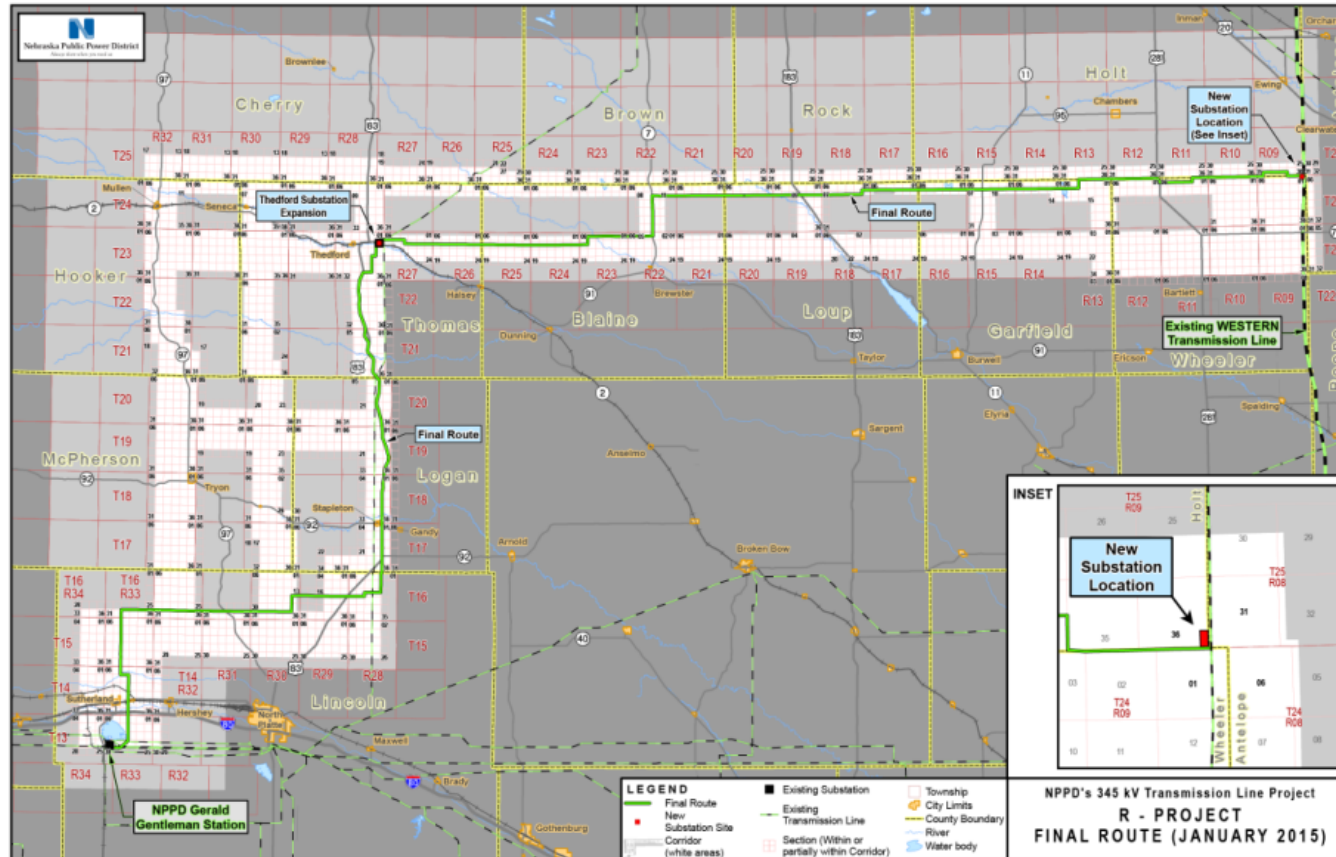

R-Project 345 kV Transmission Line

- Easement Acquisition:
 - Easement packages released for acquisition – 632 of 632 (100%)
 - Easements acquired – 427 of 632 (68%)
 - 145 of 225 miles of right-of-way acquired (64%)
 - 134 of 178 (75%) landowners have signed easements
- Continue to acquire Tension and Pull Sites
 - 38 of 51 acquired (75%)
- Continue to acquire Storage and Fly Yards
 - 21 of 26 acquired (81%)

R-Project 345 kV Transmission Line

- **The third round of Cultural Surveys were conducted from August 22-30, 2018**
- **Wetland Surveys to be conducted September 24-28, 2018**

R-Project 345 kV Transmission Line

- **Milestones:**
 - **Final Line Route Announcement – January 2015**
 - **Began Easement Acquisition – December 2015**
 - **Begin Construction – February 2019***
 - **In-service – Approximately two years after construction starts**

*No sooner than receiving record of decision from U.S. Fish & Wildlife Services

Questions?

Stay connected with us.



Nebraska Public Power District
Always there when you need us
