

Transmission Projects Update


NPPD Board of Directors
Board Meeting
July 11, 2019



Nebraska Public Power District

Always there when you need us

≡ R-Project 345 kV Transmission Line

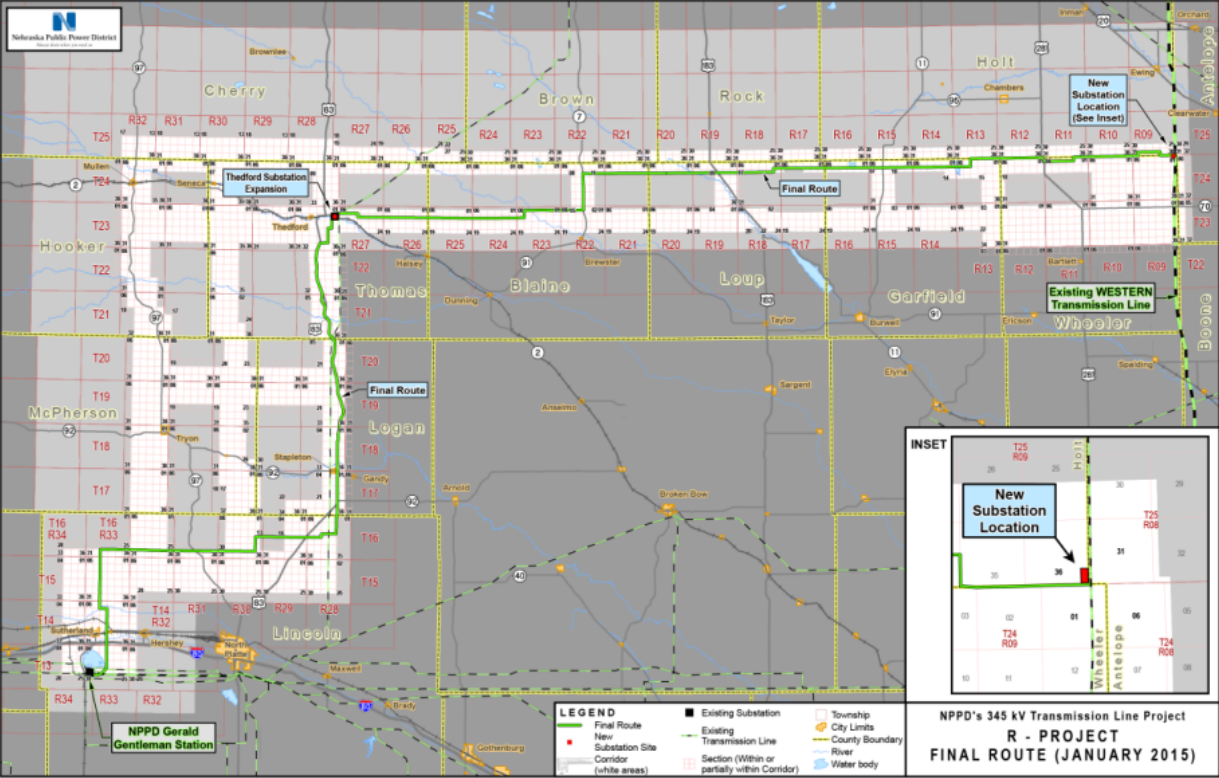

R-Project 345 kV Transmission Line

- The Record of Decision was approved and the Incidental Take Permit was issued by U.S. Fish & Wildlife Service on June 12, 2019
- U.S. Army Corps of Engineers issued NPPD a Nationwide Permit (NWP) 12 on June 27, 2019

R-Project 345 kV Transmission Line

- Next Steps:
 - Working with Forbes Bros. Timberline Construction, Inc., on a construction work plan
 - NPPD continues to contact and update remaining landowners
 - Over 80% of those remaining landowners have been recently contacted directly by NPPD since receiving the Record of Decision approval and the Incidental Take Permit
 - NPPD will continue to negotiate for voluntary easements

R-Project 345 kV Transmission Line

- Easement Acquisition:
 - Easement packages released for acquisition – 634 of 634 (100%)
 - Easements acquired – 438 of 634 (69%)
 - 147.5 of 225 miles of right-of-way acquired (66%)
 - 139 of 178 (78%) landowners have signed easements
- Continue to acquire Tension and Pull Sites
 - 39 of 52 acquired (75%)
- Continue to acquire Storage and Fly Yards
 - 23 of 26 acquired (88%)

R-Project 345 kV Transmission Line

- Completed the Western Prairie Fringed Orchid surveys on June 26, 2019

R-Project 345 kV Transmission Line

- Milestones:
 - Final Line Route Announcement – January 2015
 - Began Easement Acquisition – December 2015
 - Begin preliminary field activities – July 2019
 - Begin construction activities – Working with Forbes Bros. Timberline Construction, Inc., on schedule
 - In-service – Approximately two years after construction starts

Questions?

Stay connected with us.



Nebraska Public Power District

Always there when you need us
